




























































| ID | WBS      | Task Mode  | Task Name                      | Duration         | Start              | Finish              | Predecessors | Resource Names     | Work           |
|----|----------|--|--------------------------------|------------------|--------------------|---------------------|--------------|--------------------|----------------|
| 0  | <b>0</b> |   | <b>Projekti</b>                | <b>20,5 days</b> | <b>Mon 10.9.18</b> | <b>Mon 5.11.18</b>  |              |                    | <b>356 hrs</b> |
| 1  | <b>1</b> |   | <b>Aloitus</b>                 | <b>2 days</b>    | <b>Mon 10.9.18</b> | <b>Thu 13.9.18</b>  |              |                    | <b>24 hrs</b>  |
| 2  | 1.1      |   | Aloituskokouksen valmistelu    | 1 day            | Mon 10.9.18        | Tue 11.9.18         |              | Leena              | 8 hrs          |
| 3  | 1.2      |   | Aloituskokouksen pitäminen     | 1 day            | Wed 12.9.18        | Thu 13.9.18         | 2            | Adrian;Antti       | 16 hrs         |
| 4  | 2        |   | Tietokannan suunnittelu        | 2 days           | Fri 14.9.18        | Wed 19.9.18         | 3            | Adrian;Leena       | 32 hrs         |
| 5  | <b>3</b> |   | <b>Tietokannan luonti</b>      | <b>2,5 days</b>  | <b>Thu 20.9.18</b> | <b>Wed 26.9.18</b>  |              |                    | <b>20 hrs</b>  |
| 6  | 3.1      |   | Taulukoiden luonti             | 1 day            | Thu 20.9.18        | Fri 21.9.18         | 4            | Antti              | 8 hrs          |
| 7  | 3.2      |   | Yhteyksien luonti              | 1 day            | Mon 24.9.18        | Tue 25.9.18         | 6            | Leena              | 8 hrs          |
| 8  | 3.3      |   | Tietojen syöttö                | 0,5 days         | Wed 26.9.18        | Wed 26.9.18         | 7            | Adrian             | 4 hrs          |
| 9  | <b>4</b> |   | <b>Muiden objektien luonti</b> | <b>7 days</b>    | <b>Thu 27.9.18</b> | <b>Tue 16.10.18</b> |              |                    | <b>152 hrs</b> |
| 10 | 4.1      |   | Lomakkeiden luonti             | 3 days           | Thu 27.9.18        | Thu 4.10.18         | 8            | Adrian;Antti;Leena | 72 hrs         |
| 11 | 4.2      |  | Kyselyiden luonti              | 2 days           | Fri 5.10.18        | Wed 10.10.18        | 10           | Leena              | 16 hrs         |


Project: Projekti  
Date: Thu 23.8.18

|                    |   |                       |   |                    |   |
|--------------------|---|-----------------------|---|--------------------|---|
| Task               |  | Inactive Summary      |  | External Tasks     |  |
| Split              |  | Manual Task           |  | External Milestone |  |
| Milestone          |  | Duration-only         |  | Deadline           |  |
| Summary            |  | Manual Summary Rollup |  | Progress           |  |
| Project Summary    |  | Manual Summary        |  | Manual Progress    |  |
| Inactive Task      |  | Start-only            |  |                    |   |
| Inactive Milestone |  | Finish-only           |  |                    |   |


| ID | WBS | Task Mode   | Task Name                | Duration      | Start               | Finish             | Predecessors | Resource Names    | Work          |
|----|-----|---|--------------------------|---------------|---------------------|--------------------|--------------|-------------------|---------------|
| 12 | 4.3 |  | Raporttien luonti        | 4 days        | Fri 5.10.18         | Tue 16.10.18       | 10           | Adrian;Antti      | 64 hrs        |
| 13 | 5   |  | Tarkastuspiste           | 0 days        | Tue 16.10.18        | Tue 16.10.18       | 12           |                   | 0 hrs         |
| 14 | 6   |  | Kokoaminen sovellukseksi | 2 days        | Wed 17.10.18        | Mon 22.10.18       | 13           | Adrian;Antti;Leen | 48 hrs        |
| 15 | 7   |  | Testaus                  | 1 day         | Tue 23.10.18        | Wed 24.10.18       | 14           | Adrian;Antti      | 16 hrs        |
| 16 | 8   |  | Korjailut                | 1 day         | Thu 25.10.18        | Fri 26.10.18       | 15           | Adrian;Leena      | 16 hrs        |
| 17 | 9   |  | <b>Käyttöönotto</b>      | <b>2 days</b> | <b>Mon 29.10.18</b> | <b>Thu 1.11.18</b> |              |                   | <b>24 hrs</b> |
| 18 | 9.1 |  | Asennus                  | 1 day         | Mon 29.10.18        | Tue 30.10.18       | 16           | Leena             | 8 hrs         |
| 19 | 9.2 |  | Koulutus                 | 1 day         | Wed 31.10.18        | Thu 1.11.18        | 18           | Adrian;Antti      | 16 hrs        |
| 20 | 10  |  | Lopetus                  | 1 day         | Fri 2.11.18         | Mon 5.11.18        | 19           | Adrian;Antti;Leen | 24 hrs        |

Project: Projekti  
Date: Thu 23.8.18

|                    |   |                       |   |                    |   |
|--------------------|---|-----------------------|---|--------------------|---|
| Task               |  | Inactive Summary      |  | External Tasks     |  |
| Split              |  | Manual Task           |  | External Milestone |  |
| Milestone          |  | Duration-only         |  | Deadline           |  |
| Summary            |  | Manual Summary Rollup |  | Progress           |  |
| Project Summary    |  | Manual Summary        |  | Manual Progress    |  |
| Inactive Task      |  | Start-only            |  |                    |   |
| Inactive Milestone |  | Finish-only           |  |                    |   |

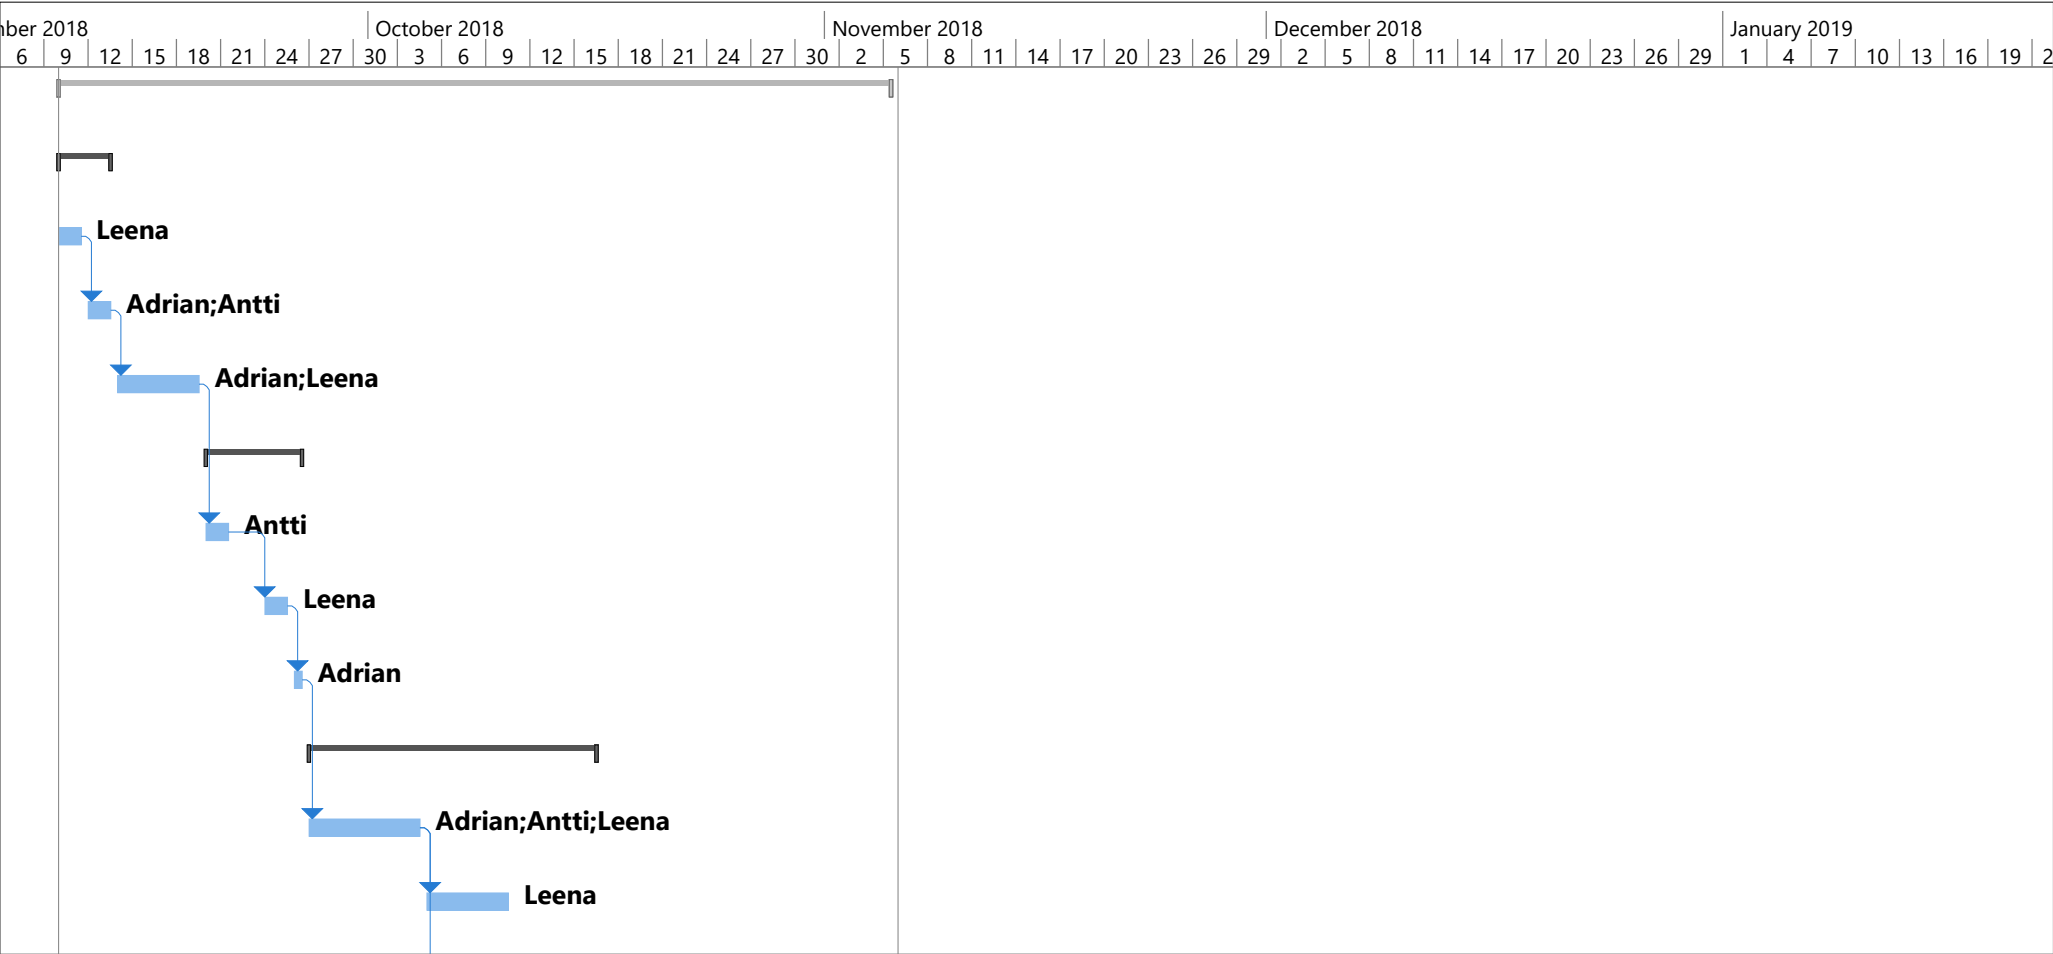

|  |                    |  |                       |  |                    |  |
|--|--------------------|--|-----------------------|--|--------------------|--|
| Project: Projekti<br>Date: Thu 23.8.18 | Task               |  | Inactive Summary      |  | External Tasks     |  |
|  | Split              |  | Manual Task           |  | External Milestone |  |
|  | Milestone          |  | Duration-only         |  | Deadline           |  |
|  | Summary            |  | Manual Summary Rollup |  | Progress           |  |
|  | Project Summary    |  | Manual Summary        |  | Manual Progress    |  |
|  | Inactive Task      |  | Start-only            |  |                    |  |
|  | Inactive Milestone |  | Finish-only           |  |                    |  |

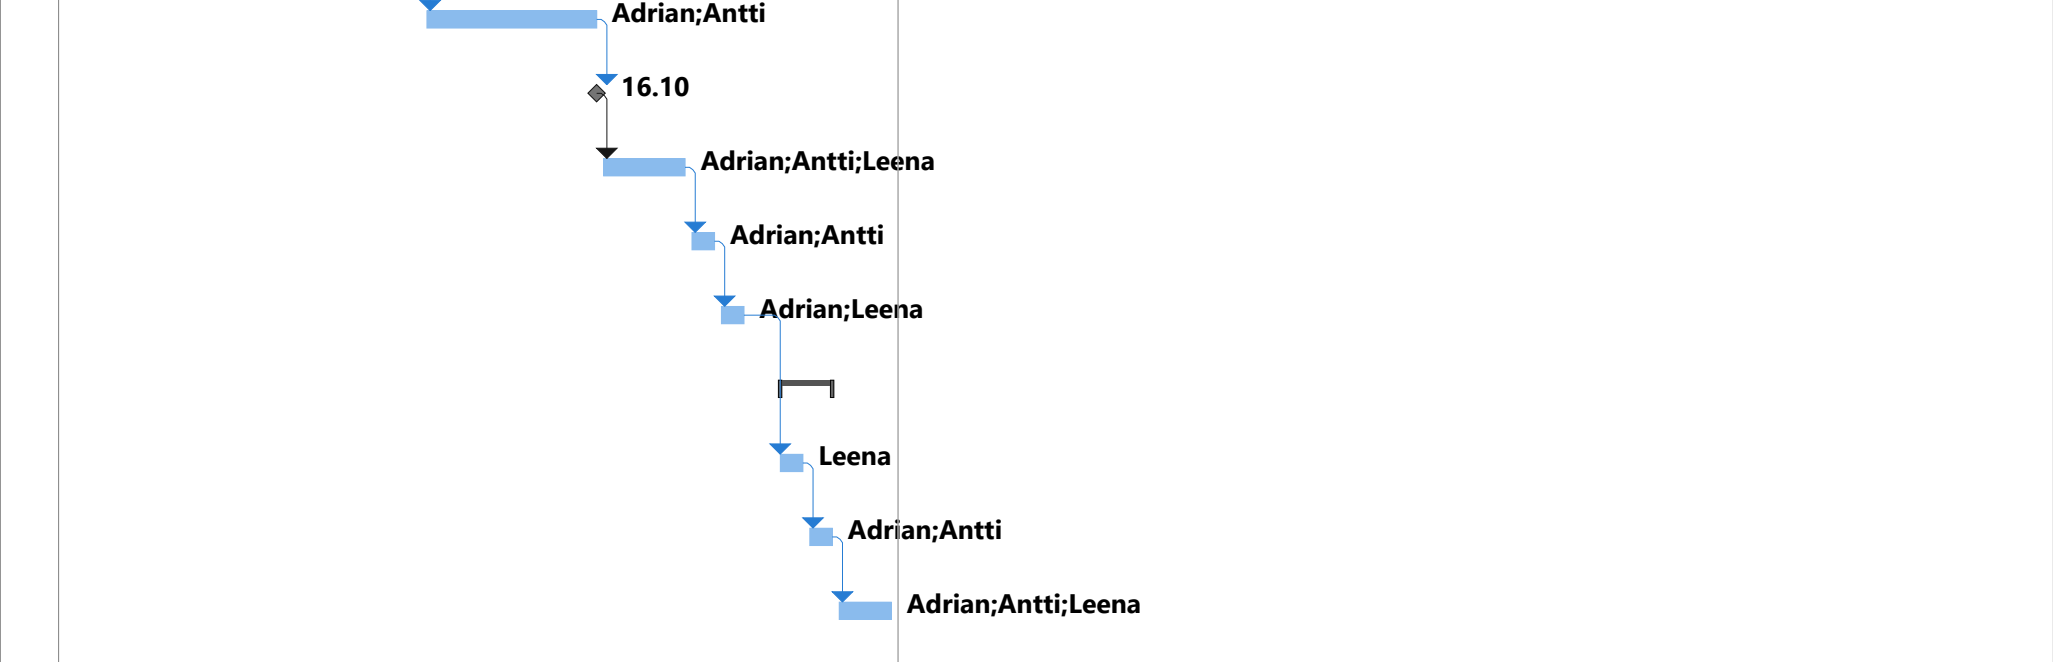

|  |                    |  |                       |  |                    |  |
|--|--------------------|--|-----------------------|--|--------------------|--|
| Project: Projekti<br>Date: Thu 23.8.18 | Task               |  | Inactive Summary      |  | External Tasks     |  |
|  | Split              |  | Manual Task           |  | External Milestone |  |
|  | Milestone          |  | Duration-only         |  | Deadline           |  |
|  | Summary            |  | Manual Summary Rollup |  | Progress           |  |
|  | Project Summary    |  | Manual Summary        |  | Manual Progress    |  |
|  | Inactive Task      |  | Start-only            |  |                    |  |
|  | Inactive Milestone |  | Finish-only           |  |                    |  |
